

ID		Task Mode	Task Name	Duration	Start	01 January			
						23-11	18-01	14-03	01 Ma 09
0			Indonesian Danone Institute Foundation Team	920 days	Mon 25-04-16				
1			Site_002 Errv Yudhya Mulvani Preparation	379 days	Mon 25-04-16				
2			a. Ethical Clearance	134 days	Thu 09-06-16				
3			1). Preparation and arrangement for EC	104 days	Thu 09-06-16				
4			2). Taking for EC letter	30 days	Wed 21-09-16				
5			b. Permitting the study site	235 days	Mon 25-04-16				
6			1). Permit from government (Kantor Walikota Jakarta Barat)	88 days	Mon 25-04-16				
7			2). Permit from Puskesmas Kecamatan Kebon Jeruk	3 days	Fri 22-07-16				
8			3). Small meeting (Coord.Meeting) with Puskesmas	123 days	Mon 15-08-16				
9			c. Preparation of completing the instrument	134 days	Fri 22-07-16				
10			1). Small Meeting (Research team)	76 days	Fri 22-07-16				
11			2). Revised Instrument	80 days	Wed 03-08-16				
12			3). Instrument multiplication	107 days	Thu 18-08-16				
13			d. Recruitment Field Worker (Enumerator)	61 days	Sat 01-10-16				























Project: Indonesian Danone Ins
Date: Fri 26-05-17























Task		Manual Task		Deadline	
Split		Duration-only		Baseline	
Milestone		Manual Summary Rollup		Baseline Milestone	
Summary		Manual Summary		Baseline Summary	
Project Summary		Start-only		Progress	
Inactive Task		Finish-only		Manual Progress	
Inactive Milestone		External Tasks		Baseline 1	
Inactive Summary		External Milestone			


ID	Task Mode	Task Name	Duration	Start	01 January			
					23-11	18-01	14-03	01 Ma 09
14		e. Training for Field Worker and Coord.Teams (Puskesmas. Laboran. and Research team)	16 days	Thu 01-12-16				
15		f. Permitting the study site for another place	97 days	Wed 01-02-17				
16		1). Permit from government (Kantor Walikota Jakarta Barat)	59 days	Wed 01-02-17				
17		2). Permit from Puskesmas Kecamatan Palmerah	11 days	Fri 28-04-17				
18		3). Small meeting (Coord.Meeting) with Puskesmas	11 days	Fri 28-04-17				
19		Data collection	682 days	Mon 19-12-16				
20		Step 1	224 days	Mon 19-12-16				
21		a. Screening Process	47 days	Mon 19-12-16				
22		1) Characteristics Subject	47 days	Mon 19-12-16				
23		2) Hydration status	47 days	Mon 19-12-16				
24		3) Dietary Intake	47 days	Mon 19-12-16				
25		4) Water Intake	47 days	Mon 19-12-16				
26		5) Maternal medical history	47 days	Mon 19-12-16				
27		6) Infant Growth	47 days	Mon 19-12-16				

Project: Indonesian Danone Ins
Date: Fri 26-05-17

Task		Manual Task		Deadline	
Split		Duration-only		Baseline	
Milestone		Manual Summary Rollup		Baseline Milestone	
Summary		Manual Summary		Baseline Summary	
Project Summary		Start-only		Progress	
Inactive Task		Finish-only		Manual Progress	
Inactive Milestone		External Tasks		Baseline 1	
Inactive Summary		External Milestone			

ID		Task Mode	Task Name	Duration	Start	01 January			
						23-11	18-01	14-03	01 Ma 09
28			7) Urine and Blood Analysis	47 days	Mon 19-12-16				
29			b. Observation Process	152 days	Wed 01-03-17				
30			1) Hydration status	122 days	Wed 01-03-17				
31			2) Dietary Intake	122 days	Wed 01-03-17				
32			3) Water Intake	122 days	Wed 01-03-17				
33			4) Maternal medical history	122 days	Wed 01-03-17				
34			5) Infant Growth	62 days	Tue 30-05-17				
35			6) Urine and Blood Analysis	122 days	Wed 01-03-17				
36			7) 8-OHdG level	122 days	Wed 01-03-17				
37			8) IGF-1 hormone level	62 days	Tue 30-05-17				
38			Step 2	230 days	Mon 13-02-17				
39			a. Screening Process	47 days	Mon 13-02-17				
40			1) Characteristics Subject	47 days	Mon 13-02-17				
41			2) Hydration status	47 days	Mon 13-02-17				

Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

ID		Task Mode	Task Name	Duration	Start	01 January			
						23-11	18-01	14-03	01 Ma 09
42			3) Dietary Intake	47 days	Mon 13-02-17				
43			4) Water Intake	47 days	Mon 13-02-17				
44			5) Maternal medical history	47 days	Mon 13-02-17				
45			6) Infant Growth	47 days	Mon 13-02-17				
46			7) Urine and Blood Analysis	47 days	Mon 13-02-17				
47			b. Observation Process	153 days	Mon 01-05-17				
48			1) Hydration status	91 days	Mon 01-05-17				
49			2) Dietary Intake	91 days	Mon 01-05-17				
50			3) Water Intake	91 days	Mon 01-05-17				
51			4) Maternal medical history	91 days	Mon 01-05-17				
52			5) Infant Growth	63 days	Sun 30-07-17				
53			6) Urine and Blood Analysis	91 days	Mon 01-05-17				
54			7) 8-OHdG level	91 days	Mon 01-05-17				
55			8) IGF-1 hormone level	63 days	Sun 30-07-17				

Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	01 January			
					23-11	18-01	14-03	01 Ma 09
56		Step 3	235 days	Mon 10-04-17				
57		a. Screening Process	47 days	Mon 10-04-17				
58		1) Characteristics Subject	47 days	Mon 10-04-17				
59		2) Hydration status	47 days	Mon 10-04-17				
60		3) Dietary Intake	47 days	Mon 10-04-17				
61		4) Water Intake	47 days	Mon 10-04-17				
62		5) Maternal medical history	47 days	Mon 10-04-17				
63		6) Infant Growth	47 days	Mon 10-04-17				
64		7) Urine and Blood Analysis	47 days	Mon 10-04-17				
65		b. Observation Process	153 days	Sat 01-07-17				
66		1) Hydration status	92 days	Sat 01-07-17				
67		2) Dietary Intake	92 days	Sat 01-07-17				
68		3) Water Intake	92 days	Sat 01-07-17				
69		4) Maternal medical history	92 days	Sat 01-07-17				
















Project: Indonesian Danone Ins
Date: Fri 26-05-17























Task		Manual Task		Deadline	
Split		Duration-only		Baseline	
Milestone		Manual Summary Rollup		Baseline Milestone	
Summary		Manual Summary		Baseline Summary	
Project Summary		Start-only		Progress	
Inactive Task		Finish-only		Manual Progress	
Inactive Milestone		External Tasks		Baseline 1	
Inactive Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	01 January			
					23-11	18-01	14-03	01 Ma 09
70		5) Infant Growth	62 days	Sat 30-09-17				
71		6) Urine and Blood Analysis	92 days	Sat 01-07-17				
72		7) 8-OHdG level	92 days	Sat 01-07-17				
73		8) IGF-1 hormone level	62 days	Sat 30-09-17				
74		Step 4	210 days	Mon 05-06-17				
75		a. Screening Process	57 days	Mon 05-06-17				
76		1) Characteristics Subject	57 days	Mon 05-06-17				
77		2) Hydration status	57 days	Mon 05-06-17				
78		3) Dietary Intake	57 days	Mon 05-06-17				
79		4) Water Intake	57 days	Mon 05-06-17				
80		5) Maternal medical history	57 days	Mon 05-06-17				
81		6) Infant Growth	57 days	Mon 05-06-17				
82		7) Urine and Blood Analysis	57 days	Mon 05-06-17				
83		b. Observation Process	122 days	Fri 01-09-17				

Project: Indonesian Danone Ins
Date: Fri 26-05-17

Task		Manual Task		Deadline	
Split		Duration-only		Baseline	
Milestone		Manual Summary Rollup		Baseline Milestone	
Summary		Manual Summary		Baseline Summary	
Project Summary		Start-only		Progress	
Inactive Task		Finish-only		Manual Progress	
Inactive Milestone		External Tasks		Baseline 1	
Inactive Summary		External Milestone			

ID		Task Mode	Task Name	Duration	Start	01 January			
						23-11	18-01	14-03	01 Ma 09
84			1) Hydration status	61 days	Fri 01-09-17				
85			2) Dietary Intake	61 days	Fri 01-09-17				
86			3) Water Intake	61 days	Fri 01-09-17				
87			4) Maternal medical history	61 days	Fri 01-09-17				
88			5) Infant Growth	62 days	Tue 31-10-17				
89			6) Urine and Blood Analysis	61 days	Fri 01-09-17				
90			7) 8-OHdG level	61 days	Fri 01-09-17				
91			8) IGF-1 hormone level	62 days	Tue 31-10-17				
92			Step 5	237 days	Mon 07-08-17				
93			a. Screening Process	54 days	Mon 07-08-17				
94			1) Characteristics Subject	54 days	Mon 07-08-17				
95			2) Hydration status	54 days	Mon 07-08-17				
96			3) Dietary Intake	54 days	Mon 07-08-17				
97			4) Water Intake	54 days	Mon 07-08-17				

Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	01 January			
					23-11	18-01	14-03	01 Ma 09
98		5) Maternal medical history	54 days	Mon 07-08-17				
99		6) Infant Growth	54 days	Mon 07-08-17				
100		7) Urine and Blood Analysis	54 days	Mon 07-08-17				
101		b. Observation Process	151 days	Wed 01-11-17				
102		1) Hydration status	92 days	Wed 01-11-17				
103		2) Dietary Intake	92 days	Wed 01-11-17				
104		3) Water Intake	92 days	Wed 01-11-17				
105		4) Maternal medical history	92 days	Wed 01-11-17				
106		5) Infant Growth	60 days	Wed 31-01-18				
107		6) Urine and Blood Analysis	92 days	Wed 01-11-17				
108		7) 8-OHdG level	92 days	Wed 01-11-17				
109		8) IGF-1 hormone level	60 days	Wed 31-01-18				
110		Step 6	174 days	Mon 09-10-17				
111		a. Screening Process	53 days	Mon 09-10-17				

Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			
















ID	Task Mode	Task Name	Duration	Start	01 January			
					23-11	18-01	14-03	01 Ma 09
112		1) Characteristics Subject	53 days	Mon 09-10-17				
113		2) Hydration status	53 days	Mon 09-10-17				
114		3) Dietary Intake	53 days	Mon 09-10-17				
115		4) Water Intake	53 days	Mon 09-10-17				
116		5) Maternal medical history	53 days	Mon 09-10-17				
117		6) Infant Growth	53 days	Mon 09-10-17				
118		7) Urine and Blood Analysis	53 days	Mon 09-10-17				
119		b. Observation Process	90 days	Mon 01-01-18				
120		1) Hydration status	59 days	Mon 01-01-18				
121		2) Dietary Intake	59 days	Mon 01-01-18				
122		3) Water Intake	59 days	Mon 01-01-18				
123		4) Maternal medical history	59 days	Mon 01-01-18				
124		5) Infant Growth	59 days	Thu 01-02-18				
125		6) Urine and Blood Analysis	59 days	Mon 01-01-18				

Project: Indonesian Danone Ins
Date: Fri 26-05-17























Task		Manual Task		Deadline	
Split		Duration-only		Baseline	
Milestone		Manual Summary Rollup		Baseline Milestone	
Summary		Manual Summary		Baseline Summary	
Project Summary		Start-only		Progress	
Inactive Task		Finish-only		Manual Progress	
Inactive Milestone		External Tasks		Baseline 1	
Inactive Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	01 January			
					23-11	18-01	14-03	01 Ma 09
126		7) 8-OHdG level	59 days	Mon 01-01-18				
127		8) IGF-1 hormone level	59 days	Thu 01-02-18				
128		Step 7	209 days	Mon 04-12-17				
129		a. Screening Process	59 days	Mon 04-12-17				
130		1) Characteristics Subject	59 days	Mon 04-12-17				
131		2) Hydration status	59 days	Mon 04-12-17				
132		3) Dietary Intake	59 days	Mon 04-12-17				
133		4) Water Intake	59 days	Mon 04-12-17				
134		5) Maternal medical history	59 days	Mon 04-12-17				
135		6) Infant Growth	59 days	Mon 04-12-17				
136		7) Urine and Blood Analysis	59 days	Mon 04-12-17				
137		b. Observation Process	122 days	Thu 01-03-18				
138		1) Hydration status	92 days	Thu 01-03-18				
139		2) Dietary Intake	92 days	Thu 01-03-18				

Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

ID		Task Mode	Task Name	Duration	Start	01 January			
						23-11	18-01	14-03	01 Ma 09
140			3) Water Intake	92 days	Thu 01-03-18				
141			4) Maternal medical history	92 days	Thu 01-03-18				
142			5) Infant Growth	61 days	Tue 01-05-18				
143			6) Urine and Blood Analysis	92 days	Thu 01-03-18				
144			7) 8-OHdG level	92 days	Thu 01-03-18				
145			8) IGF-1 hormone level	61 days	Tue 01-05-18				
146			Step 8	200 days	Mon 12-02-18				
147			a. Screening Process	47 days	Mon 12-02-18				
148			1) Characteristics Subject	47 days	Mon 12-02-18				
149			2) Hydration status	47 days	Mon 12-02-18				
150			3) Dietary Intake	47 days	Mon 12-02-18				
151			4) Water Intake	47 days	Mon 12-02-18				
152			5) Maternal medical history	47 days	Mon 12-02-18				
153			6) Infant Growth	47 days	Mon 12-02-18				

Project: Indonesian Danone Ins
Date: Fri 26-05-17

Task		Manual Task		Deadline	
Split		Duration-only		Baseline	
Milestone		Manual Summary Rollup		Baseline Milestone	
Summary		Manual Summary		Baseline Summary	
Project Summary		Start-only		Progress	
Inactive Task		Finish-only		Manual Progress	
Inactive Milestone		External Tasks		Baseline 1	
Inactive Summary		External Milestone			

ID	Task Mode	Task Name	Duration	Start	01 January			
					23-11	18-01	14-03	01 Ma 09
154		7) Urine and Blood Analysis	47 days	Mon 12-02-18				
155		b. Observation Process	122 days	Tue 01-05-18				
156		1) Hydration status	92 days	Tue 01-05-18				
157		2) Dietary Intake	92 days	Tue 01-05-18				
158		3) Water Intake	92 days	Tue 01-05-18				
159		4) Maternal medical history	92 days	Tue 01-05-18				
160		5) Infant Growth	31 days	Tue 31-07-18				
161		6) Urine and Blood Analysis	92 days	Tue 01-05-18				
162		7) 8-OHdG level	92 days	Tue 01-05-18				
163		8) IGF-1 hormone level	31 days	Tue 31-07-18				
164		Step 9	206 days	Mon 09-04-18				
165		a. Screening Process	53 days	Mon 09-04-18				
166		1) Characteristics Subject	53 days	Mon 09-04-18				
167		2) Hydration status	53 days	Mon 09-04-18				














Project: Indonesian Danone Ins
Date: Fri 26-05-17


Task		Manual Task		Deadline	
Split		Duration-only		Baseline	
Milestone		Manual Summary Rollup		Baseline Milestone	
Summary		Manual Summary		Baseline Summary	
Project Summary		Start-only		Progress	
Inactive Task		Finish-only		Manual Progress	
Inactive Milestone		External Tasks		Baseline 1	
Inactive Summary		External Milestone			























ID	Task Mode	Task Name	Duration	Start	01 January			01 Ma
					23-11	18-01	14-03	
168		3) Dietary Intake	53 days	Mon 09-04-18				
169		4) Water Intake	53 days	Mon 09-04-18				
170		5) Maternal medical history	53 days	Mon 09-04-18				
171		6) Infant Growth	53 days	Mon 09-04-18				
172		7) Urine and Blood Analysis	53 days	Mon 09-04-18				
173		b. Observation Process	123 days	Sun 01-07-18				
174		1) Hydration status	92 days	Sun 01-07-18				
175		2) Dietary Intake	92 days	Sun 01-07-18				
176		3) Water Intake	92 days	Sun 01-07-18				
177		4) Maternal medical history	92 days	Sun 01-07-18				
178		5) Infant Growth	61 days	Sat 01-09-18				
179		6) Urine and Blood Analysis	92 days	Sun 01-07-18				
180		7) 8-OHdG level	92 days	Sun 01-07-18				
181		8) IGF-1 hormone level	61 days	Sat 01-09-18				

Project: Indonesian Danone Ins
Date: Fri 26-05-17

Task		Manual Task		Deadline	
Split		Duration-only		Baseline	
Milestone		Manual Summary Rollup		Baseline Milestone	
Summary		Manual Summary		Baseline Summary	
Project Summary		Start-only		Progress	
Inactive Task		Finish-only		Manual Progress	
Inactive Milestone		External Tasks		Baseline 1	
Inactive Summary		External Milestone			

ID		Task Mode	Task Name	Duration	Start	01 January			01 Ma
						23-11	18-01	14-03	
182			Data entry	365 days	Sun 01-01-17				
183			Data analysis	120 days	Sun 01-01-17				
184			Report writing	59 days	Wed 01-02-17				
185			Report submission	59 days	Wed 01-02-17				
186			Manuscript Preparation	1 day	Mon 01-05-17				
187			Publication	92 days	Mon 01-05-17				



Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

1 May 09-05 | 04-07 | 01 September 29-08 | 24-10 | 01 January 19-12 | 13-02 | 01 May 10-04 | 05-06 | 01 September 31-07 | 25-09 | 20-11 | 01 January 15-01 | 12-03 | 01 May 07-05 | 02-07 | 01 September 27-08 | 22-10 | 01 January 17-12




Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			


1 May 09-05 | 04-07 | 01 September 29-08 | 24-10 | 01 January 19-12 | 13-02 | 01 May 10-04 | 05-06 | 01 September 31-07 | 25-09 | 20-11 | 01 January 15-01 | 12-03 | 01 May 07-05 | 02-07 | 01 September 27-08 | 22-10 | 01 January 17-12




Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

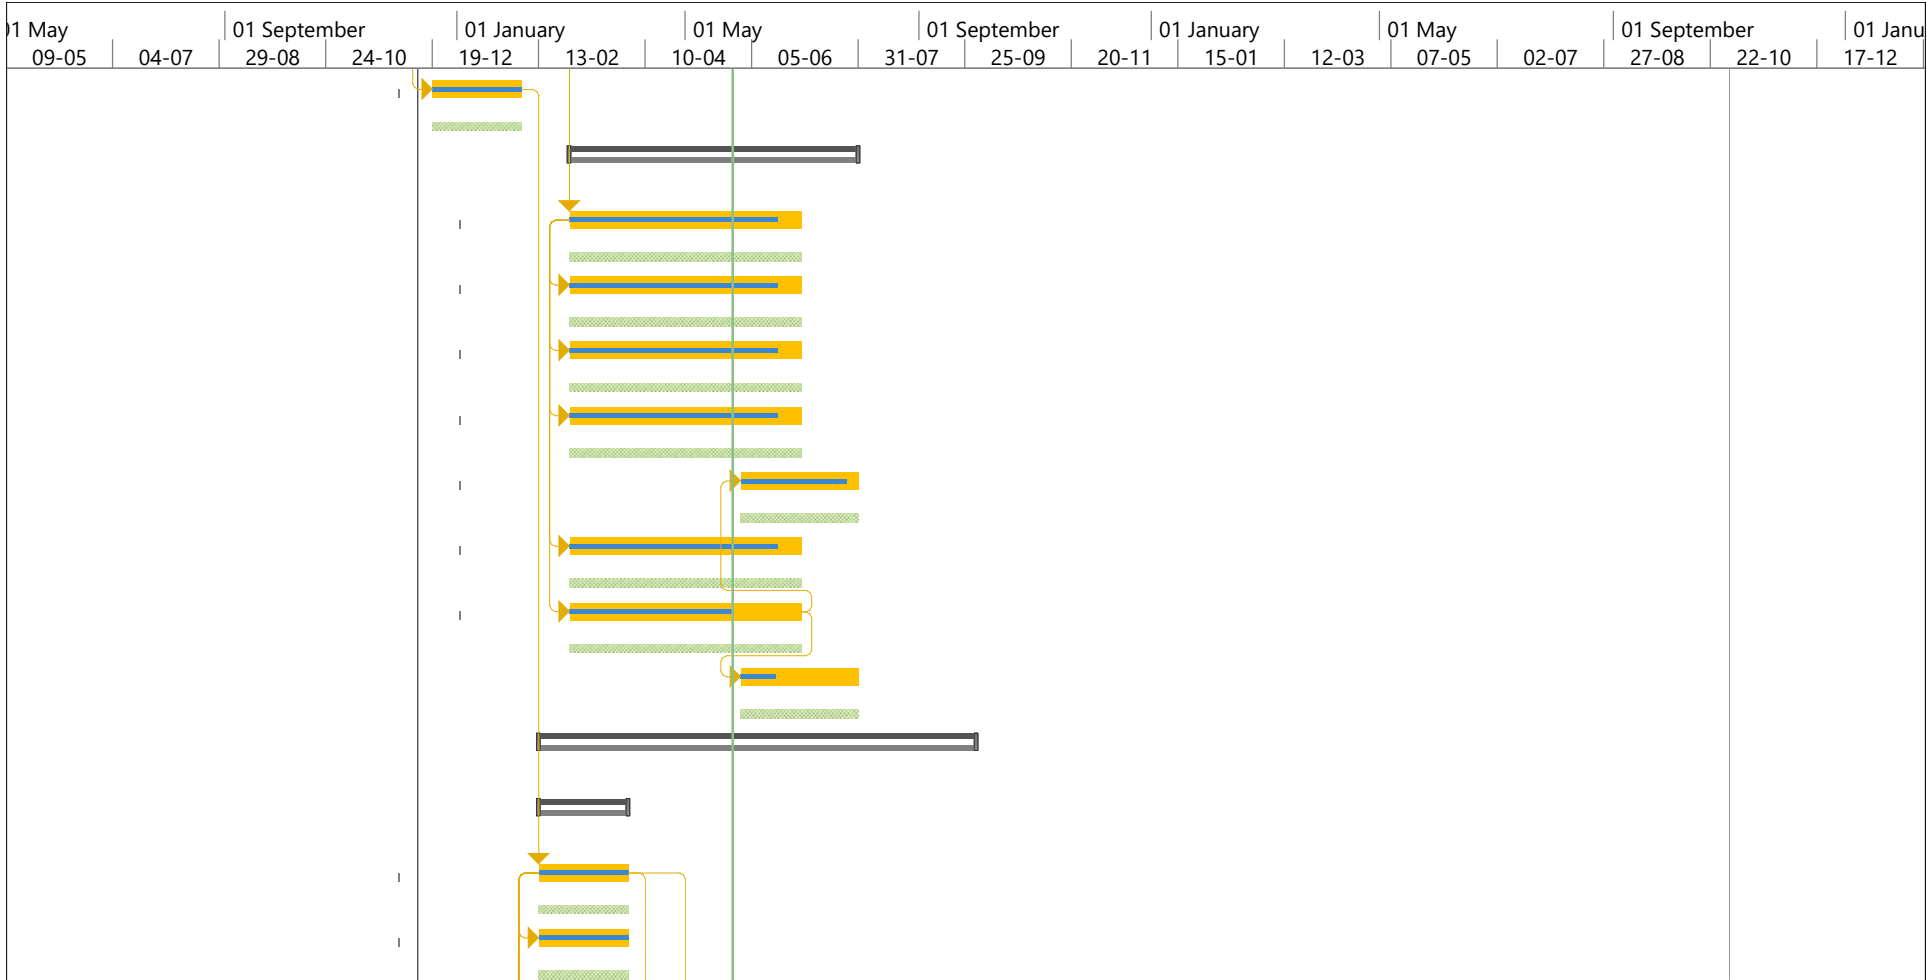


Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

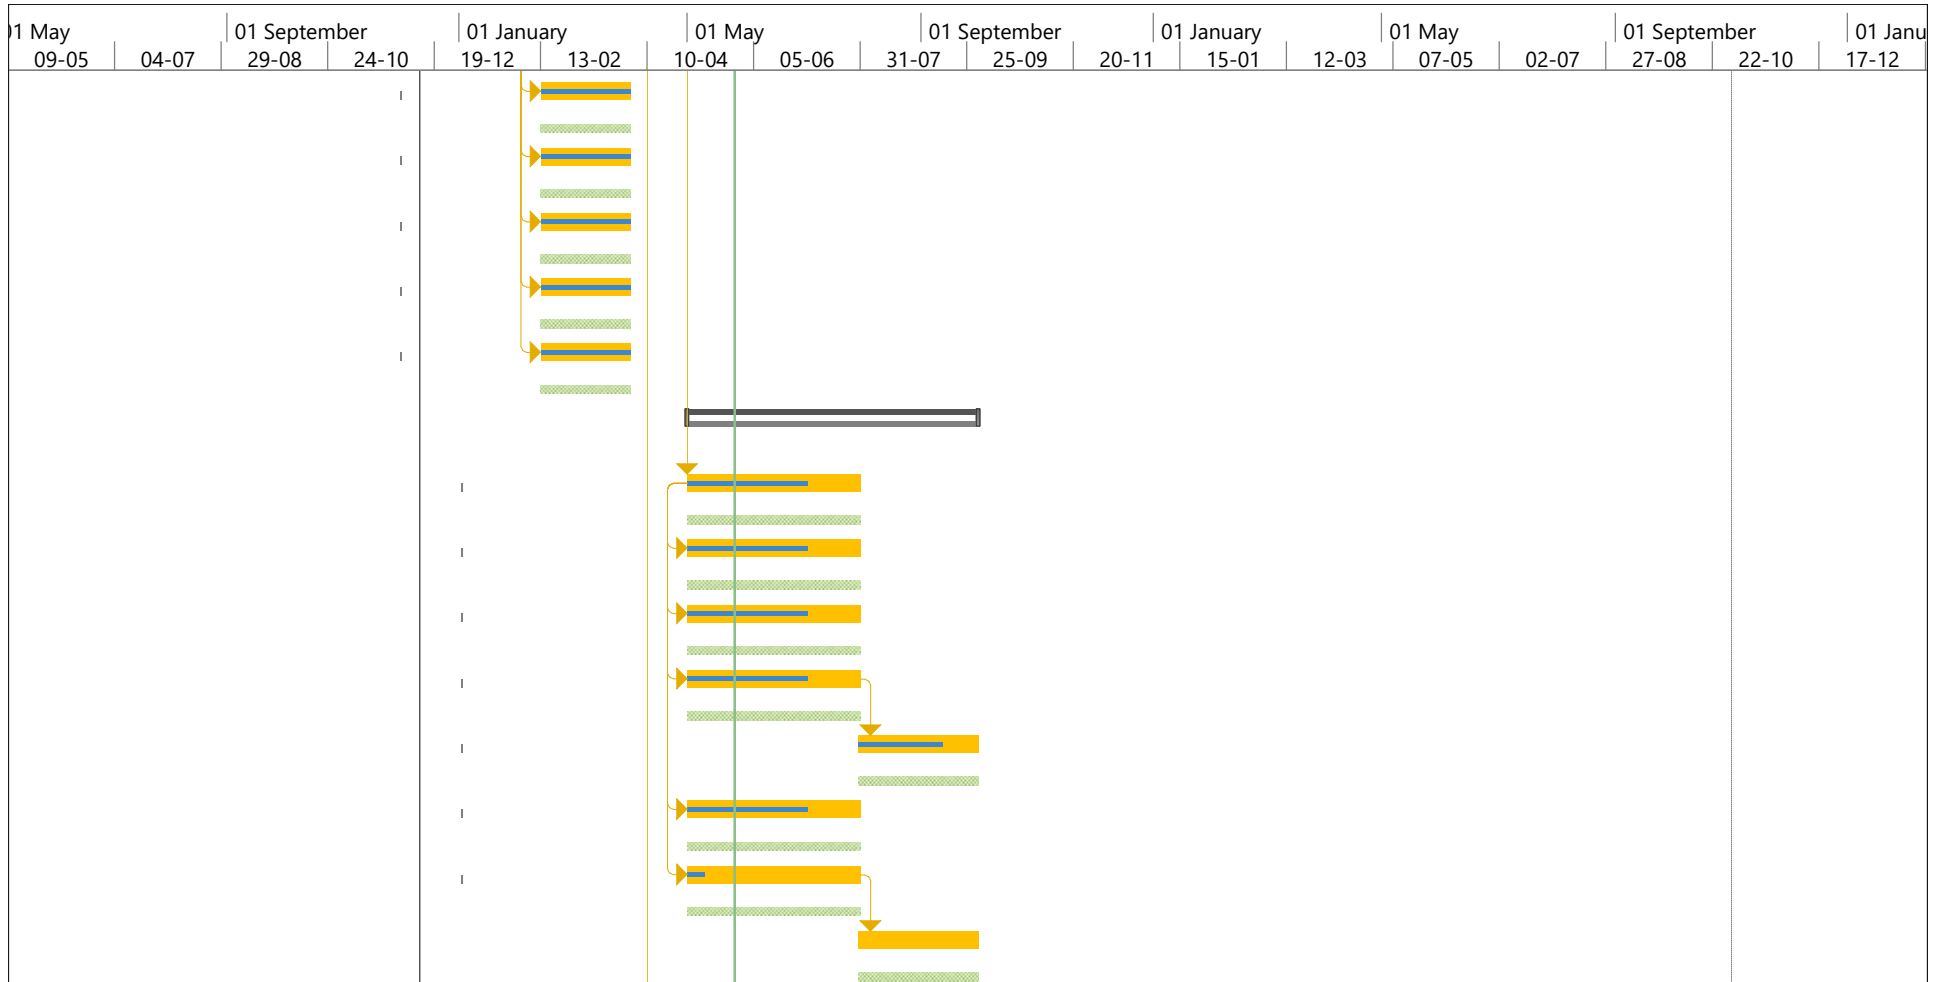

Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

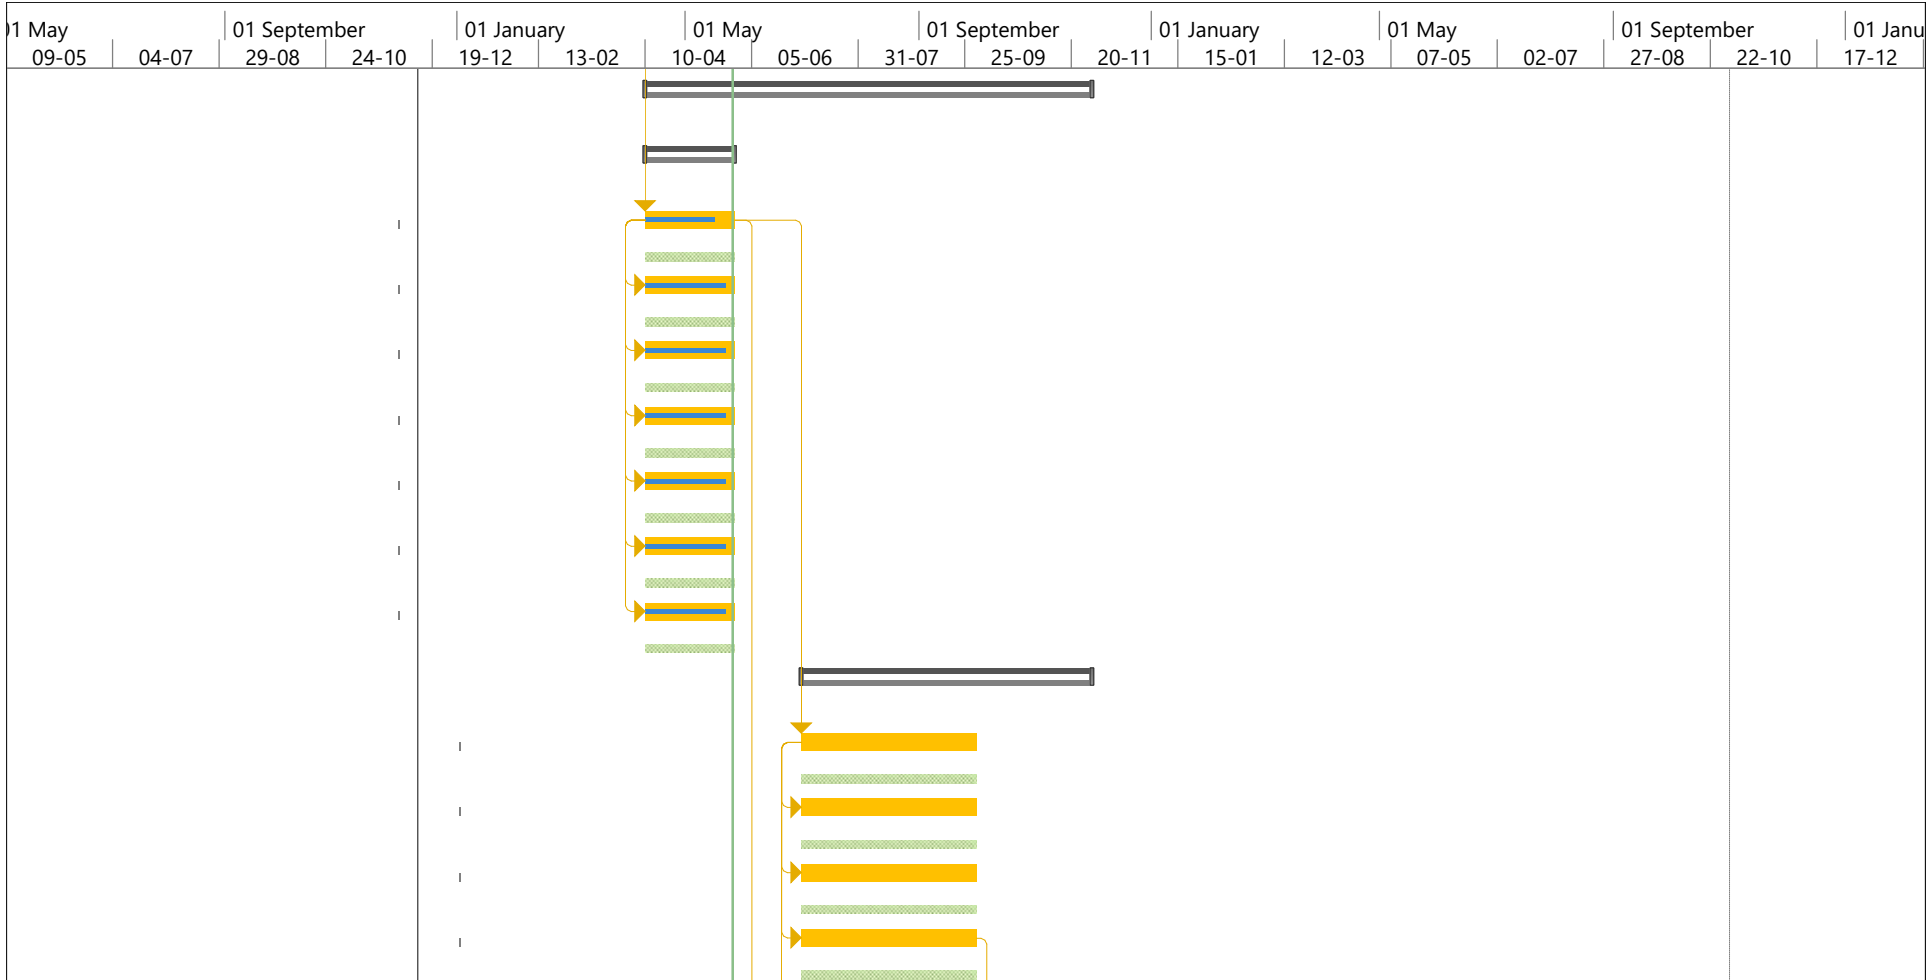


Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

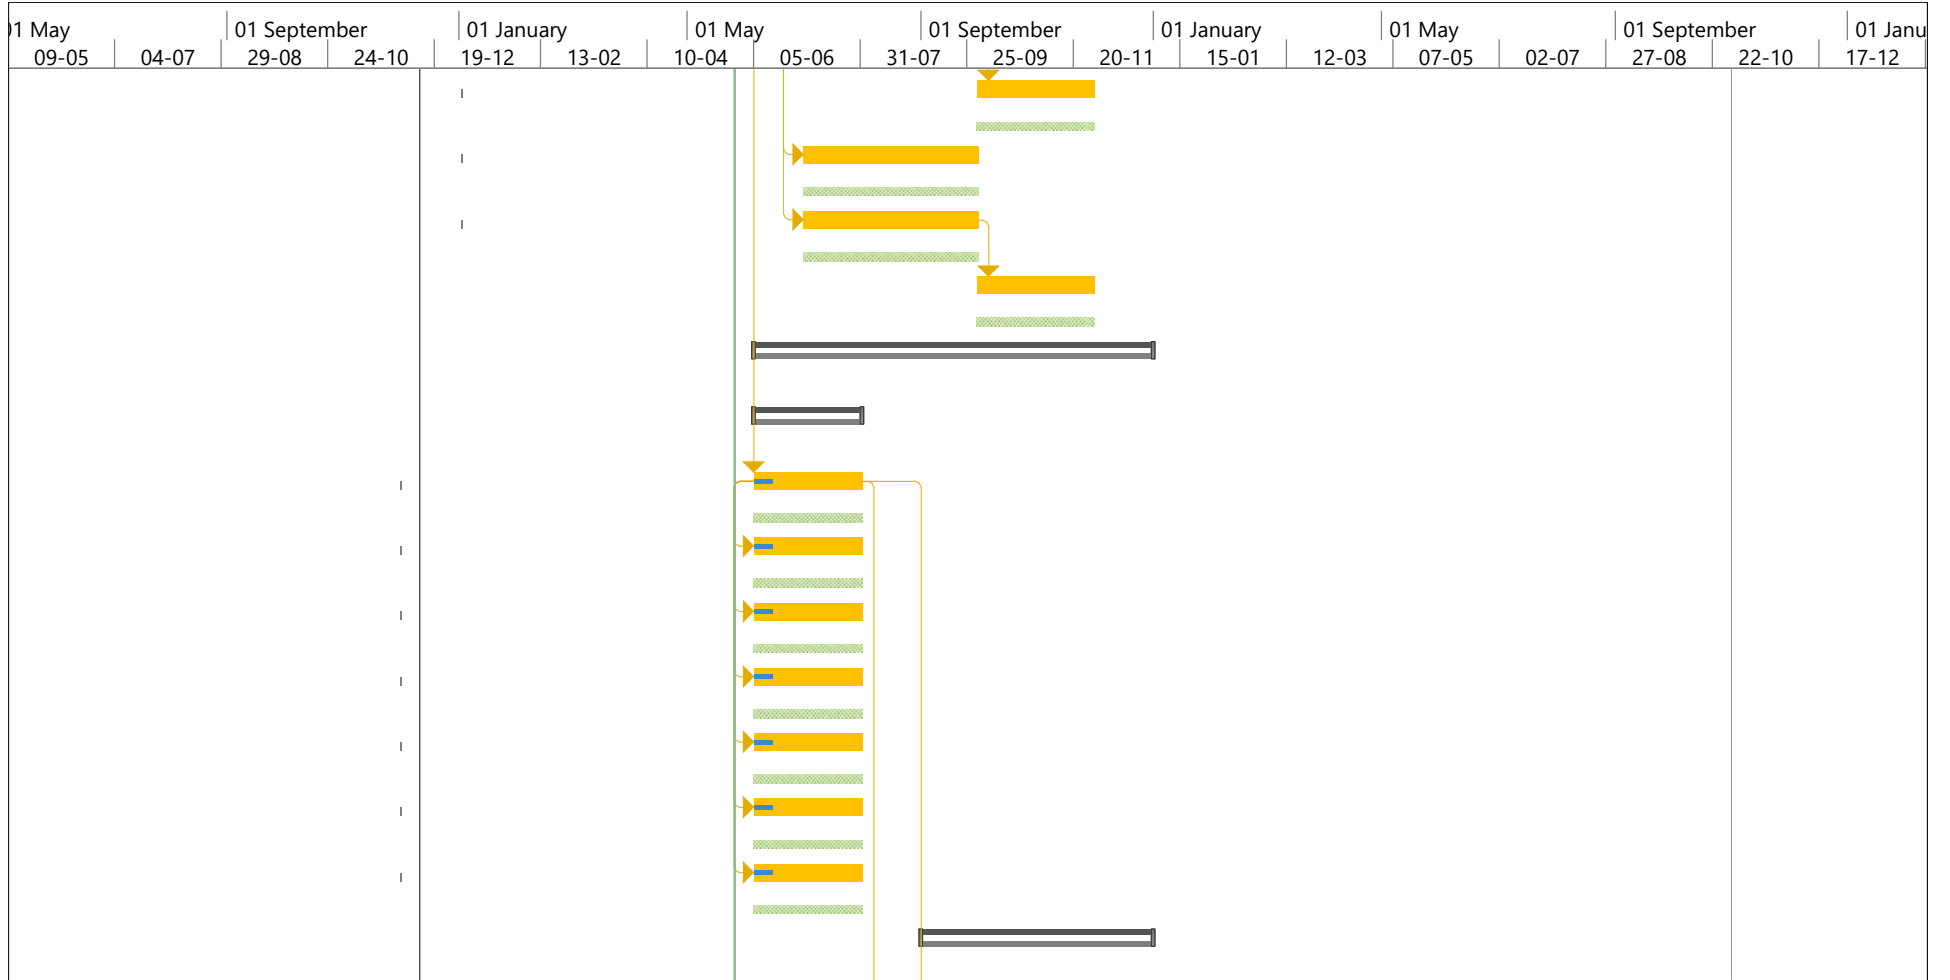


Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			




Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

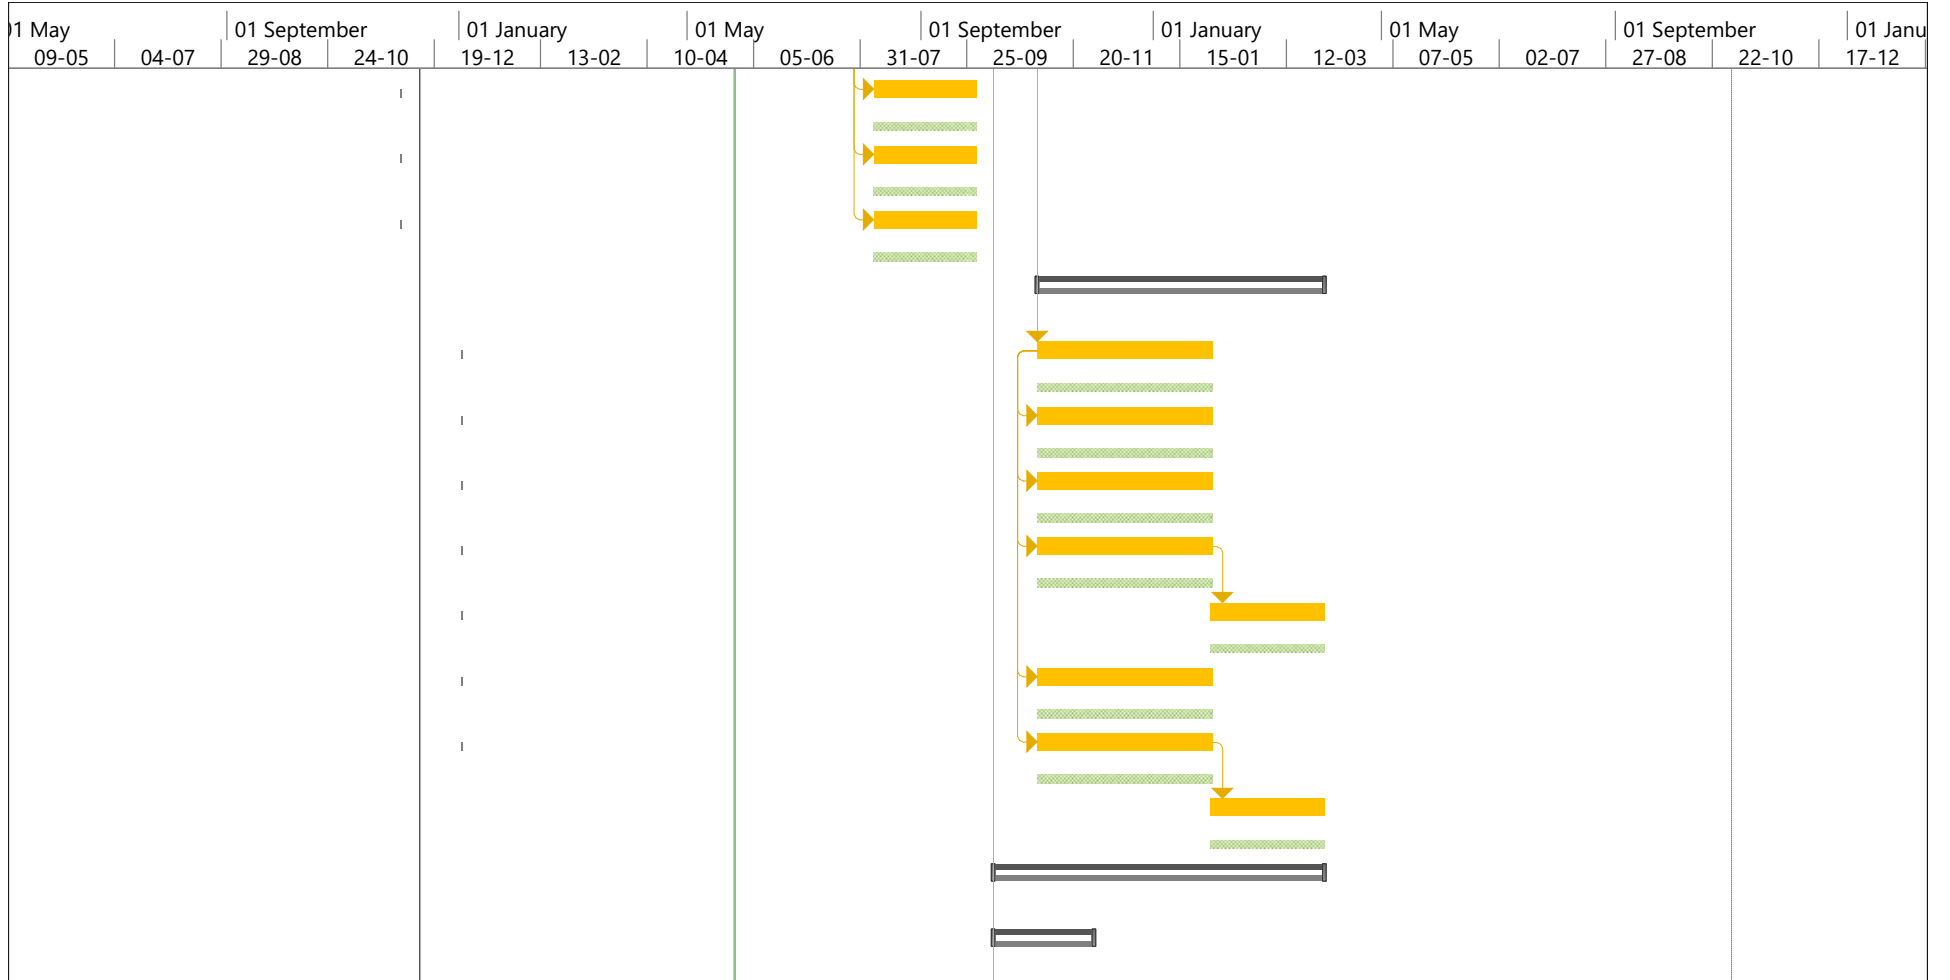


Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

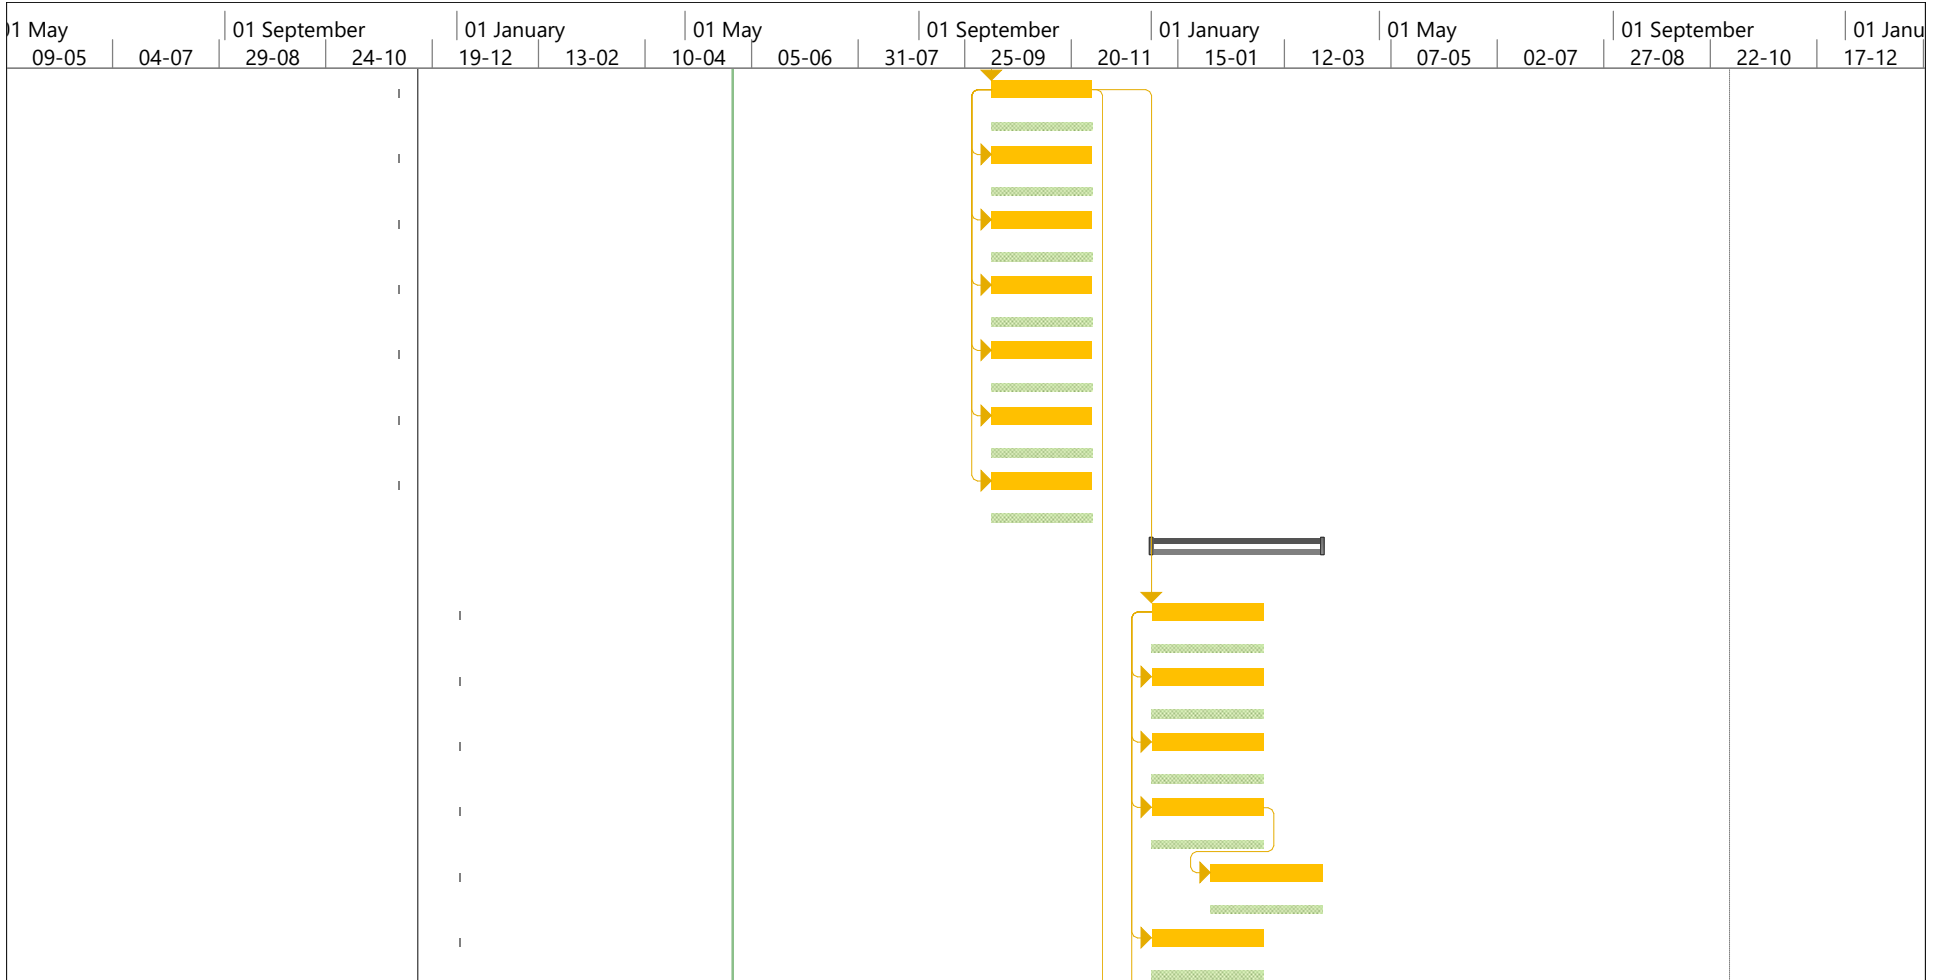


Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

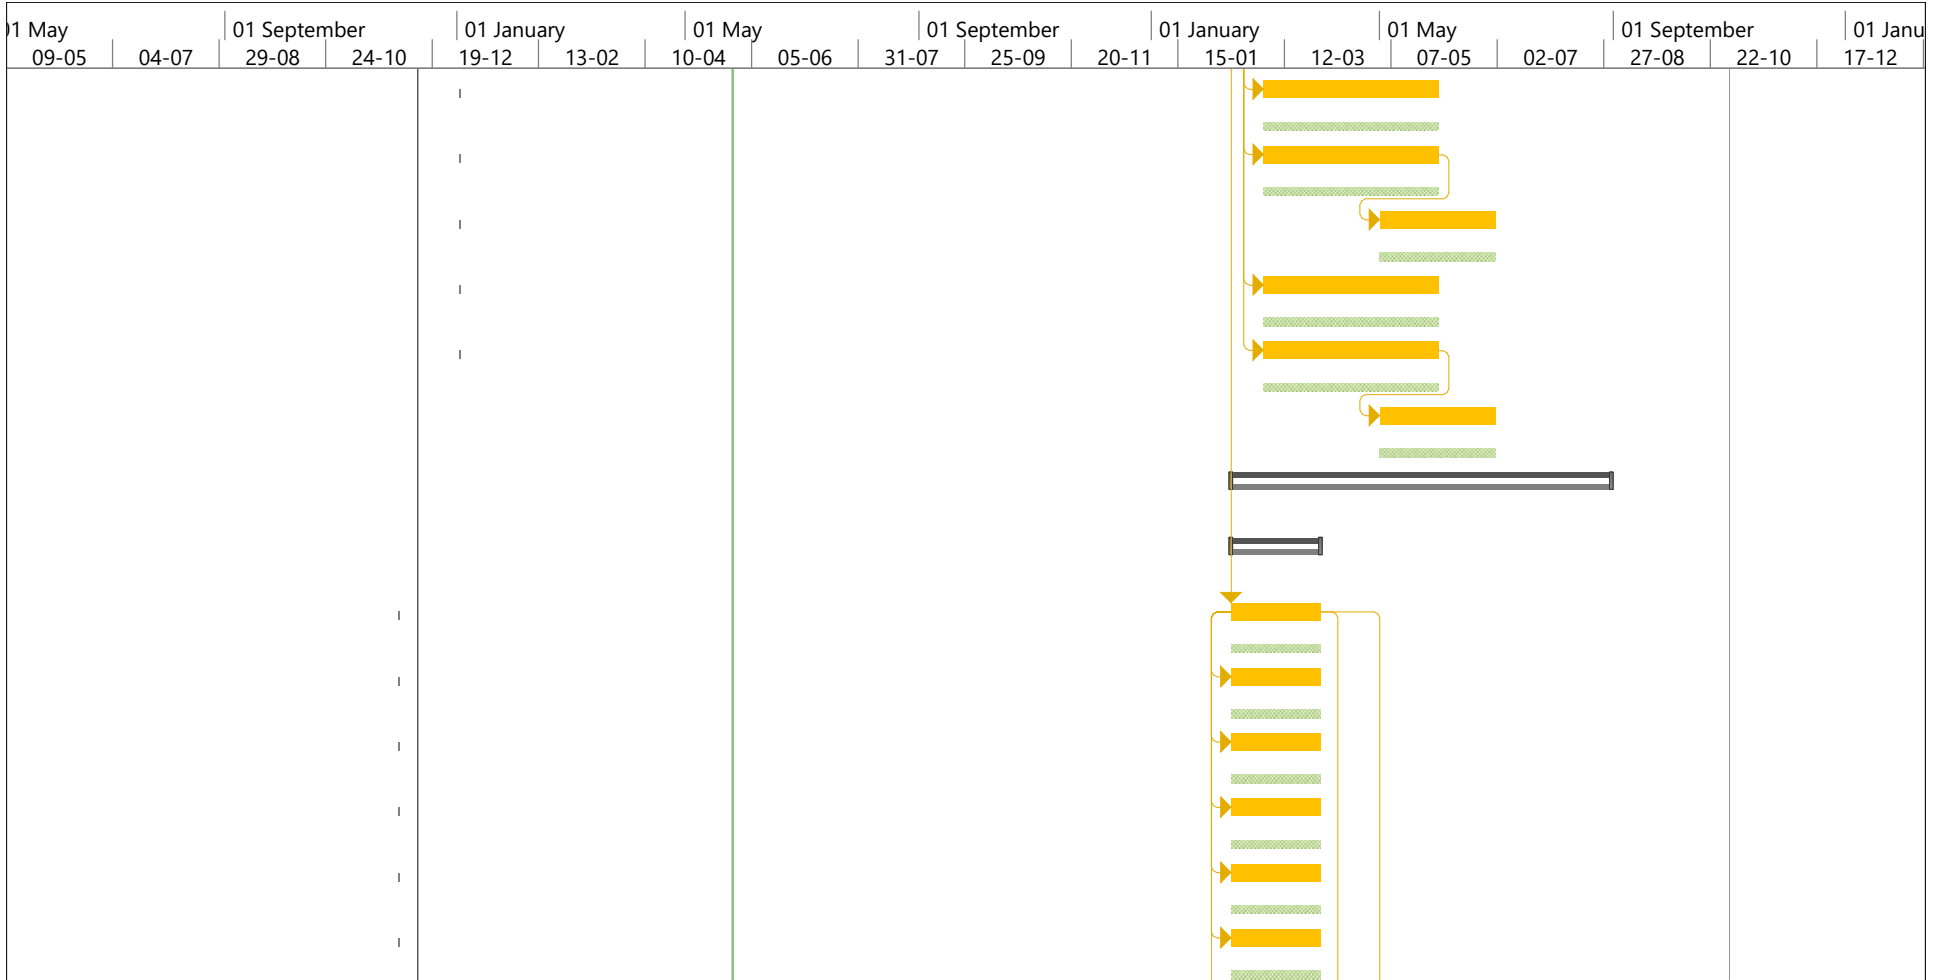

Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

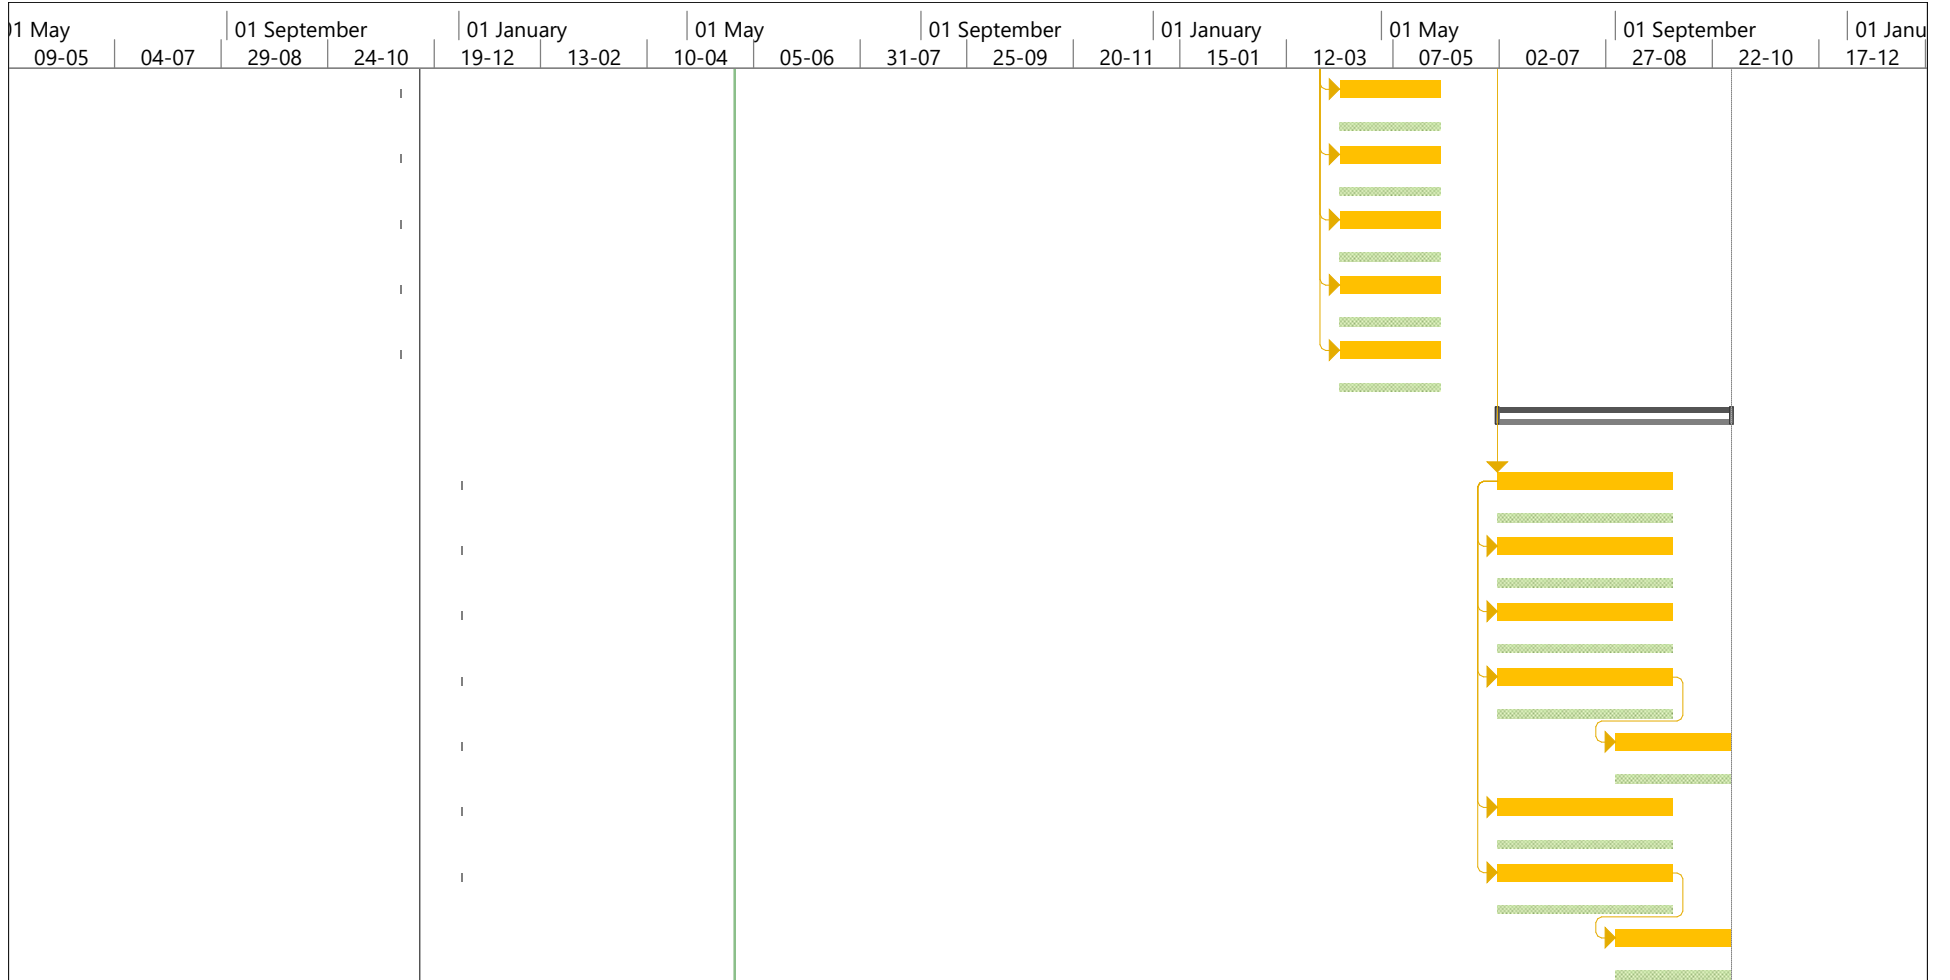

Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			

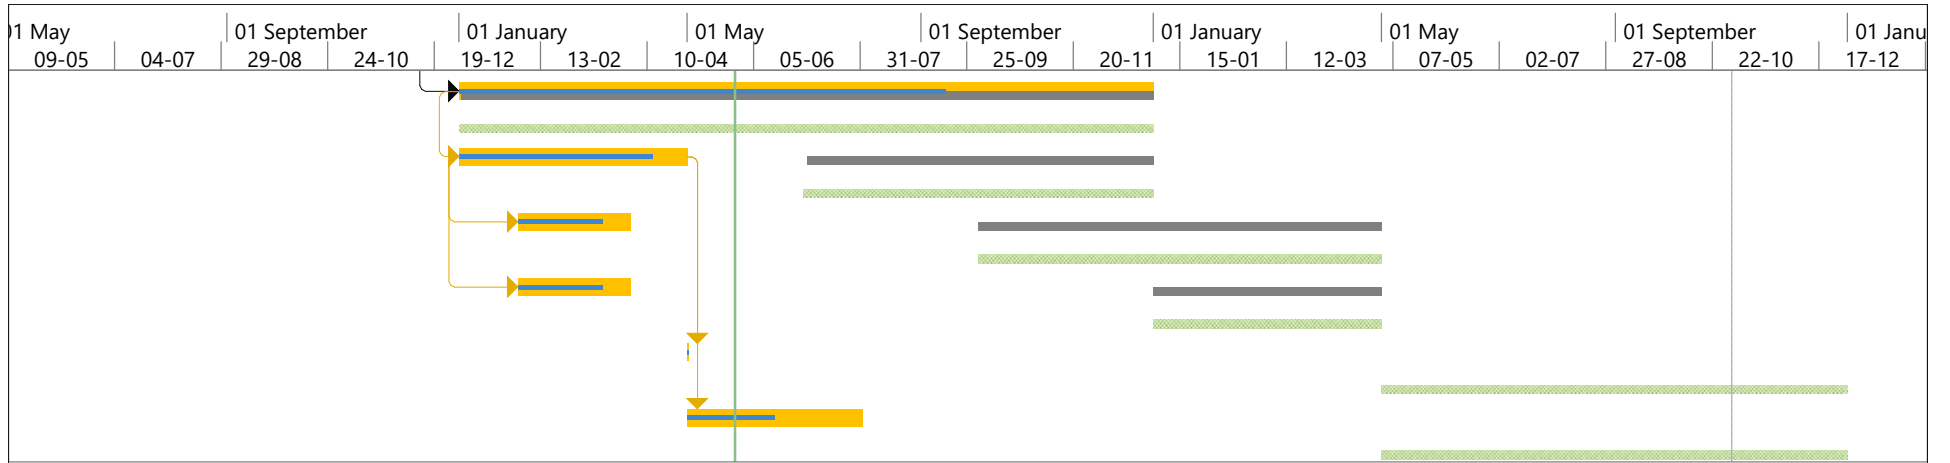

Project: Indonesian Danone Ins Date: Fri 26-05-17	Task		Manual Task		Deadline	
	Split		Duration-only		Baseline	
	Milestone		Manual Summary Rollup		Baseline Milestone	
	Summary		Manual Summary		Baseline Summary	
	Project Summary		Start-only		Progress	
	Inactive Task		Finish-only		Manual Progress	
	Inactive Milestone		External Tasks		Baseline 1	
	Inactive Summary		External Milestone			
